EXECUTIVE ONE-PAGER

FieldFlow Service Cloud (sample)

Brightwater (fictional) · Executive one-pager · Prepared by Alex Morgan

Harbour & Pine

AMBER

AS OF
23 Feb 2027

OVERALL STATUS	COMPLETE	FORECAST FINISH	MILESTONES MET	OVERDUE TASKS
Amber	48%	3 Jun 2027	3 of 7	0
Finish 13 days late	Expected 48% by now · 13 of 34 tasks done	Baseline 17 May · +13 working days	Next: SIT exit · 19 Apr	of 21 open tasks

HIGHLIGHTS

Three of 9 phases are complete. 48% complete against 48% planned, broadly on plan; 13 of 34 tasks done.

CONCERNS

Forecast finish 3 Jun 2027 is 13 working days after the baseline of 17 May 2027.


NEXT 14 DAYS

Three tasks are due in the next 14 days, including Extract legacy CRM data (Grace Okafor, 24 Feb).

DECISIONS AND SUPPORT NEEDED

No decisions requested this period.

PHASE	DONE	FINISH	STATUS
Discovery and design	100%	8 Dec 26	Done
Build and configure	100%	16 Feb	Done
Data migration	15%	5 Apr	At risk
Integrations	15%	29 Mar	At risk
Testing	0%	13 May	At risk
Training and change	0%	28 Apr	At risk
Cutover and go-live	0%	20 May	At risk
Hypercare	0%	3 Jun	At risk
OPEN MILESTONES (3 OF 7 MET)		**DUE**	**STATUS**
SIT exit		19 Apr	At risk
UAT sign-off		13 May	At risk
Go-live		20 May	At risk

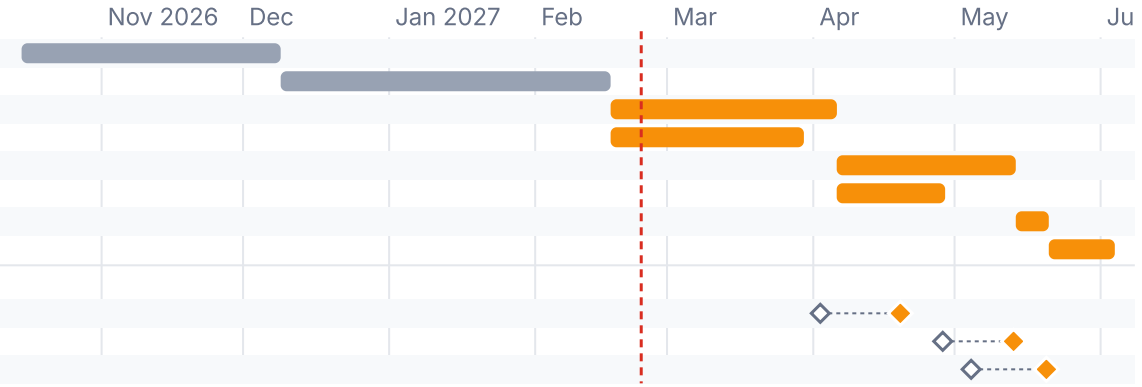

1 earlier completed phase not shown. +1 open milestone in the roadmap. Data check: 41 rows, no issues. Status rules: Amber if finish is over 5 wd past baseline, a milestone is overdue, over 3 tasks are overdue or progress is over 10 points behind; Red above 15 wd, 2 overdue milestones or 20 points. Schedule only; cost and scope not assessed.
